
Ilkeston Road Access Point Visibility Splay Requirements.

A site meeting was conducted on 23/09/2025 to review the requirements outlined in the visibility sprays and to meet the requirements.

Attendees, Rob Braddock, Smalley View Farm Director, PG Bosworth Farming contractors, WLB Tree services, Andy Roberts- Roberts Highway Consultants by virtual video.

After reviewing the site and the requiring hedgerow it was determined that in order to meet the required visibility spray below that no hedgerow requires removal or reduction in height but the hedgerows do require trimming back to permit the required siting. The red line in drawing 2 illustrates the line of site requiring trimming back. This will be carried out by our two contractors in line with Hedgerow Management rules and hedgerow regulations 19997.

Diagrams illustrating the line if site and required hedgerow to be cut back approx 1m back to its point of growth.

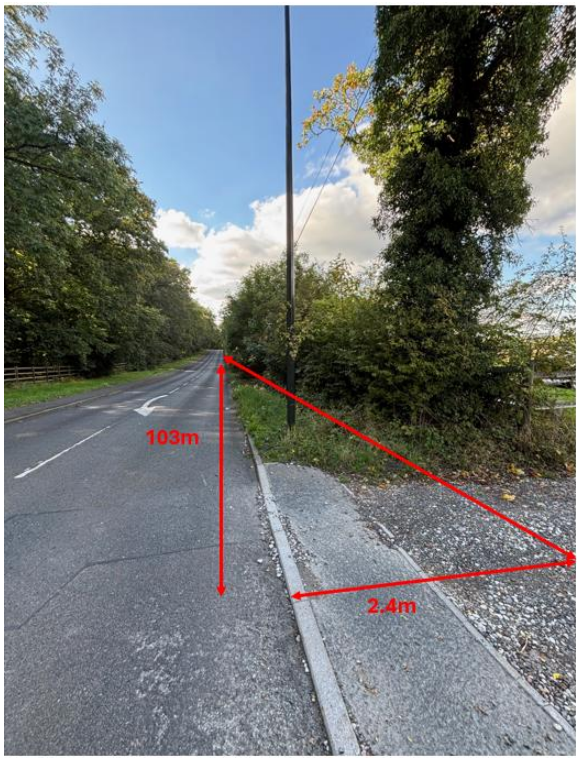



Ilkeston Road Visibility splay document 1468277 from planning application.

