AT2 Tree Surveys

Tree Survey

and

Arboricultural Method Statement

for

108A Cromford Road

Langley Mill

13th August 2026



The Stables, 14 King Street, Nether Broughton, Melton Mowbray LE14 3HA
01664 822118 / 07952 992957 info@at2treesurvey.co.uk www.at2treesurvey.co.uk

BSi 5837:2012

Contents

Contents 2
Introduction 3
Considerations 4
Damage to Trees[2] 4
Protection of trees during construction 6
Trees subject to Statutory Control 6
Trees and Wildlife 6
Implementation of Tree Works 6
Design considerations 6
Arboricultural constraints related to BS5837 grading 8
Tree Survey 9
Methodology & limitations 9
Site description 9
Recorded information 11
Tree Survey Plan 12
Survey Schedule 13
BS 5837:2012 Cascade chart for tree quality assessment 14
Arboricultural Impact Assessment (AIA) 15
Impact of the development on the trees 15
Impact of the trees on the development 15
Arboricultural Method Statement (AMS) 16
Pre-development tree work 16
Construction exclusion zones 16
Foundation construction 17
Routing of services 17
Hard surfacing 18
Other measures 19
Sequence of works 20
Monitoring 20
Appendix A – Glossary of arboricultural terms 21
Appendix B – Site guidance notes 24
Appendix C – Bibliography & References 25

© 2010-2026 All rights reserved

Introduction

AT2 was instructed by Walker Design (Nottingham) Ltd to prepare an arboricultural impact assessment with reference to the application reference AVA/2026/0329 for two self-build dwellings at 108A Cromford Road in Langley Mill. This report describes the methods to be deployed to ensure minimum impact to the retained trees.

All rights in this report are reserved. The content and format are for the exclusive use of the entity purchasing the report and only the purchaser can rely on the report. Trees are living organisms whose health and condition can change over time. Accordingly, the period of reliance is limited to four years from the date of the report. Use of this report is conditional on payment having been made within the terms of the invoice.

The report includes the following sections:

- Context of the report including the following considerations:
    - Tree physiology and potential for damage
    - The importance of protecting trees during construction
    - Trees subject to statutory controls
    - Trees and wildlife
    - Implementation of tree works
    - Design considerations
- Tree survey – provides an objective catalogue of the species, size and condition of the trees on or adjacent to a site. The results of the tree survey inform the design options.
- Arboricultural impact assessment – identifies and evaluates the direct and indirect impacts on existing trees that may arise as a result of the implementation of the design proposal.
- Arboricultural method statement – details of methodologies to be implemented in order to protect the retained trees through each stage of the development.
- Appendices
    A. Glossary of arboricultural terms
    B. Site guidance notes
    C. Bibliography & references

Arboricultural terms that are included in the glossary in appendix B will be appear in **bold** on the first occasion of their use.



© 2010-2026 All rights reserved

Considerations

Damage to Trees[2]

Having evolved slowly and gradually over millions of years, trees and their roots are not very adaptable to relatively rapidly changing human impacts and disruption that produce compaction, physical disturbance and severance. Any development activity which affects the adaptation of trees to a site could be detrimental to their health, future growth, safety and stability. Tree species differ in their ability to tolerate change but all tend to become less tolerant after they have reached maturity or suffered previous damage or stress. Planning and subsequent site management should aim to minimise the effect of change.

The part of a tree most susceptible to damage is the root system which, because it is hidden from view, is frequently ignored. Damage to, or death of the root system affects the health, growth, life expectancy and safety of the entire tree. The effects of such damage may only become evident several years later. Damage may be the result of a number of insignificant but compounding factors that accumulate over time.




Damage to the stem and branches of a tree is not usually sufficient to kill the tree directly but may make it unsafe by affecting the weight of distribution of the crown or by facilitating decay in the long term. Such damage may also be disfiguring.

Roots perform several functions:

- Anchoring the tree in the ground
- Taking up water and nutrients from the soil
- Storing food for times of dormancy

Roots grow predominantly near the soil surface – 90% or more of all roots, and virtually all of the large structural supporting roots, are within 60cm of the surface of the ground. Although they may be deeper within the dense mass of roots and soil close to the base of the tree it is uncommon for roots to penetrate to a depth greater than 2 metres[7].

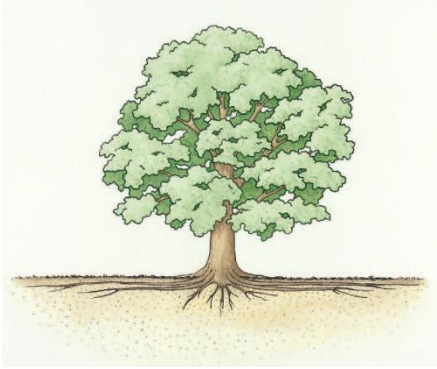

Trees have relatively shallow but wide spreading roots[6].

Within a short distance of the stem the roots are highly branched so as to form a network of small-diameter woody roots that typically extend radially for a distance much greater than the height of the tree, except where impeded by unfavourable conditions. All parts of this system bear a mass of fine, non-woody absorptive roots.

The root system does not generally show the symmetry seen in the branch system. Roots proliferate wherever they encounter favourable soil conditions which is why the greatest root concentration is found close to the soil surface where the soil is loosest, and water, oxygen and nutrients are most readily available. As far as these conditions allow, the root system tends to develop sufficient volume and area to provide physical stability.

The uptake of water and mineral nutrients by the root system takes place via the fine roots, typically less than 0.5 mm diameter. Their survival and functioning - which are essential for the health of the tree as a

© 2010-2026 All rights reserved

whole - depend on the maintenance of favourable soil conditions. The fine roots are short-lived with the majority dying each winter and with fresh ones developing in response to the needs of the tree.

All parts of the root system, but especially the fine roots, are vulnerable to damage. Once roots are damaged, water and nutrient uptake is restricted until new ones have grown. Mature and over-mature trees respond slowly, if at all, to damage of their woody roots.

The main risks to tree roots come from physical damage and compaction to the surrounding soil.

- Physical damage:

  During construction damage is often sustained when digging foundations or trenches for services. Surface roots are at risk when laying driveways, hardstanding and landscaping. Damaged roots are an entry point for infection and if a root is cut completely the tree loses a proportion of its capacity to take up water and minerals, store energy for the winter and weakens its anchorage in the ground.



Walnut roots smashed by an excavator.

- Compaction:

  This is often caused by vehicular traffic. Tree roots need oxygen to respire and growth is inhibited or stopped when the airspaces in the soil are lost through compaction.

- Other damage:

  Trees can also be damaged by contamination from fuel and chemical spillages or by fires.

Unless the damage is extremely severe it is unlikely that a tree will show symptoms immediately. More typically there is a steady decline over a few years with smaller leaves, crown dieback and possibly, eventual failure.

© 2010-2026 All rights reserved

Protection of trees during construction

BS5837: 2012 Trees in relation to design, demolition and construction - Recommendations[2] gives guidance on the implementation of protection for trees and roots before and during construction.

Recognising the importance of root health, the British Standard defines the **root protection area (RPA)** as:

> *the minimum area around a tree deemed to contain sufficient roots and rooting volume to maintain the tree's viability, and where the protection of the roots and soil structure is treated as a priority.*

The RPA is calculated as an area equivalent to a circle with a radius 12 times the stem diameter measured at a height of 1.5m above ground level. Any modifications to the shape of the RPA should only be made based on a sound arboricultural assessment of likely root distribution.

The tree survey schedule on page 13 gives the radius of the RPA for each tree. This is the minimum distance at which barriers should be stationed to protect trees and their roots to form a **construction exclusion zone (CEZ)**.

Trees subject to Statutory Control

Local Planning Authorities may assess trees as beneficial to the wider community in terms of their amenity value. They may protect such trees with a Tree Preservation Order (TPO). Work may still be permitted on protected trees but permission for the works must first be obtained from the LPA.

Some areas are designated conservation areas. Before carrying out works on a tree in a conservation area notice must be given to the LPA. The LPA can either allow the works to proceed or impose a TPO.

Where felling would produce more than five cubic metres of timber a felling license may be required from the Forestry Commission. However, this does not apply to trees growing in an orchard, garden, churchyard or public open space.

Trees and Wildlife

Trees are hosts to nesting birds and mammals. Under the Wildlife and Countryside Act it is an offence to disturb any nesting bird or bat. Before carrying out any works it is important to ensure that there are no birds or bats in residence.

Implementation of Tree Works

Tree work is skilled and potentially dangerous. Work should be carried out by trained and certificated contractors working to BS 3998: 2010 *Recommendations for Tree work*[1].



Design considerations

The default position should be that structures are located outside the RPAs of trees to be retained[2]. However, where there is an overriding justification for construction within the RPA, technical solutions might be available that prevent damage to the trees such as pile and beam foundations and permeable geocells. In such circumstances, in addition to installing a technical solution, the RPA shape should be modified to ensure that the total area protected without damage is at least equivalent to the original RPA size.

On shrink/swell clay soils, trees and other vegetation have the potential to cause indirect damage to structures. Soil structure, composition and moisture (desiccation) levels should be assessed for

© 2010-2026 All rights reserved

foundation design to take account of retained, removed and new trees, and to inform any new planting design.

The relationship of buildings to large trees can cause apprehension to occupiers or users of nearby buildings or spaces, resulting in pressure for the removal of the trees. Buildings and other structures should be designed and/or sited with due consideration given to the trees' ultimate height and canopy spread. The design should take into account future growth so as to reduce the need for frequent remedial pruning or other maintenance.

Shading and light penetration should also be considered when positioning windows and indoor and outdoor living spaces to allow sufficient natural light. This survey does not include any shade assessment although it is possible to model the shade cast by tree canopies at different times of the day and year.

Where permanent hard surfacing within the RPA is considered unavoidable, new hard surfacing should be gas and water permeable and should not require excavation into the soil ("**no-dig**"). BS5837 recommends that new hard surfacing should not exceed 20% of any existing unsurfaced ground within the RPA[2].

Early consultation and collaboration regarding the planning of utility runs is recommended so that underground services can be combined in a single trench that avoids the RPA.

To fulfil their potential, trees need to reach maturity. Many newly planted trees fail to survive the first two years due to inadequate ground preparation and lack of aftercare. In some studies, after 22 years only 42% had survived, putting long-term canopy cover and ecological service targets at risk.

Environmental legislation is evolving. The Environment Act 2021 and the Town and Country Planning Act set targets for biodiversity net gain whilst the NPPF (National Planning Policy Framework) sets the objective of sustainable development including:

- Existing trees are retained wherever possible (paragraph 136)
- New streets are tree-lined, opportunities are taken to incorporate trees elsewhere in developments and that appropriate measures are in place to secure the long-term maintenance of newly-planted trees (paragraph 136)
- Opportunities to improve biodiversity in and around developments should be integrated as part of their design. (paragraph 186.d)



Fastigiate oaks and planes on a Dutch street.

Over the long-term, larger, long-lived trees have lower annual maintenance costs and give much greater benefit. Where practical, landscape design should diverge from the limited palette of cherry, birch and rowan and consider varieties of larger species. A diverse mix of planting will help provide resilience against future pests and diseases. Guidelines recommended that the mix contains no more than 30% from the same family, 20% from the same genus and 10% of the same species.

Retaining mature trees may also increase property values. Several studies have shown that average house prices are between 5% and 18% higher where property is associated with mature trees (NUFU 2005).

The Trees & Design Action Group publishes a number of free guides designed to facilitate a better understanding of the range of returns that trees offer new developments and how to secure these returns.

© 2010-2026 All rights reserved

Arboricultural constraints related to BS5837 grading

The survey schedule on page 13 includes a tree quality assessment grading in accordance with BS5837. Trees are graded as A, B, C or U in accordance with the assessment cascade chart on page 14.

- Trees identified as category A are those of high quality with an estimated remaining life expectancy of at least 40 years. These trees are particularly good examples of their species or of particular visual importance as arboricultural and/or landscape features. They pose a significant constraint to development and should be retained, protected and incorporated within the design where possible. Category A trees are shaded green on the tree plan.



- Trees identified as category B are those of moderate quality with an estimated remaining life expectancy of at least 20 years. These are trees that might be included in category A, but are downgraded because of impaired condition (e.g. presence of significant though remediable defects, including unsympathetic past management and storm damage). They also pose a significant constraint to development and should be retained, protected and incorporated within the design where possible. Category B trees are shaded blue on the tree plan.



- Trees identified as category C are those of low quality with an estimated remaining life expectancy of at least 10 years. These are unremarkable trees offering low or only temporary/transient landscape benefits. They are in an adequate condition to be retained but could be replaced by new planting. Category C includes young trees with a stem diameter below 150mm which are not yet of a size to make a significant contribution to the landscape. These trees should not be considered to pose a significant constraint to development but should be retained and protected where possible. Category C trees are shaded grey on the tree plan.



- Trees identified as category U are those in such a condition that they cannot realistically be retained as living trees in the context of the current land use for longer than 10 years. This includes trees that have a serious structural defect, trees that are dead or are showing signs of significant overall decline and very low-quality trees suppressing adjacent trees of better quality. These trees are unsuitable for retention and should not be a constraint to development. Category U trees are shaded red on the tree plan.



N.B. Biodiversity net gain (BNG) scores trees according to their ecological value which may conflict with the BS5837 gradings. Low quality trees graded C or U may have high ecological value and score highly for BNG.

© 2010-2026 All rights reserved

Tree Survey

Methodology & limitations

The trees were inspected from ground level to produce a catalogue of species, size and general condition and their longer-term value. The soil was not examined and no samples were taken for analysis. There has been no attempt to determine whether the soil is shrinkable.

The content of the tree survey should be used to inform the design options. It is not intended to be used as a detailed tree risk management survey. Trees are living organisms whose health and condition can change rapidly and no guarantee can be given as to the absolute safety or otherwise of any tree. The report may include some recommendations to reduce the likelihood of tree failure but absolute safety is not a realistic goal; even apparently sound trees can fail, particularly during extreme weather – best practice recommends that trees are inspected every 18 months when they are alternately in and out of leaf[13].

The position of the trees on the plan on page 12 is not intended to infer ownership which should be clarified before any tree work is carried out.

Site description



The entrance to the site looking northeast from Cromford Road.

The site is an overgrown area of land to the east of Cromford Road. The aerial imagery suggests it was part of a large area of allotments but it has been uncultivated for many years. More recently the goat willow was coppiced but this has started to grow back. The Amber Valley District Council website does not indicate that the site is within a conservation area and but it is understood that the neighbouring lime tree (T1) is protected by a tree preservation order TPO 308/2004. A tree plan is included on page 12 showing canopies shaded in accordance with their BS5837 categories and their root protection areas coloured magenta. At the time of the visit the weather was fine and sunny.

© 2010-2026 All rights reserved



Goat willow regrowth in the middle of the site.

© 2010-2026 All rights reserved

Recorded information

The following details were recorded for each tree and tabulated in the survey schedule:


- Tree plan ID; G prefix denotes group of trees.
- Species; Common name and *botanical name.*
- Height in metres measured using a Nikon 550 Forestry Pro hypsometer.
- Girth and diameter measured at 1.5 metres above ground level (# denotes estimated measurement where trunk is inaccessible; typ. ⇒ typical value).
- Whether the tree has a single or multiple stems.
- The calculated radius in metres for the **root protection area** (shown in magenta in the tree survey plan on page 12).
- The cardinal spread of the crown in metres.
- Canopy height in metres (ground clearance).
- The height in metres to the crown break (height of the lowest branches on the main trunk).
- The life stage:
    - Young: establishing, usually with good vitality but as yet of limited significance in the landscape.
    - Semi-mature: established, normally vigorous, increasing in height and of increasing landscape significance.
    - Early-mature: established; approaching mature height with crown spreading.
    - Mature: fully established trees around the middle of their typical life expectancy; generally retaining good vitality and achieving full height but their crowns still spreading.
    - Over-mature: fully established trees toward the end of their typical life expectancy with declining vitality.
    - Ancient: surviving beyond the typical age range for the species. Very old with low vitality and liable to decline. May include important Veteran Trees.
- Physiological and structural condition including the presence of physical defects and decay.
- Estimated remaining contribution in years.
- Tree quality assessment grading in accordance with BS5837:2012 (see page 14).

For expediency some trees may have less detail recorded and, in some cases, similar trees may be grouped for the purposes of this survey.



© 2010-2026 All rights reserved

Tree Survey Plan

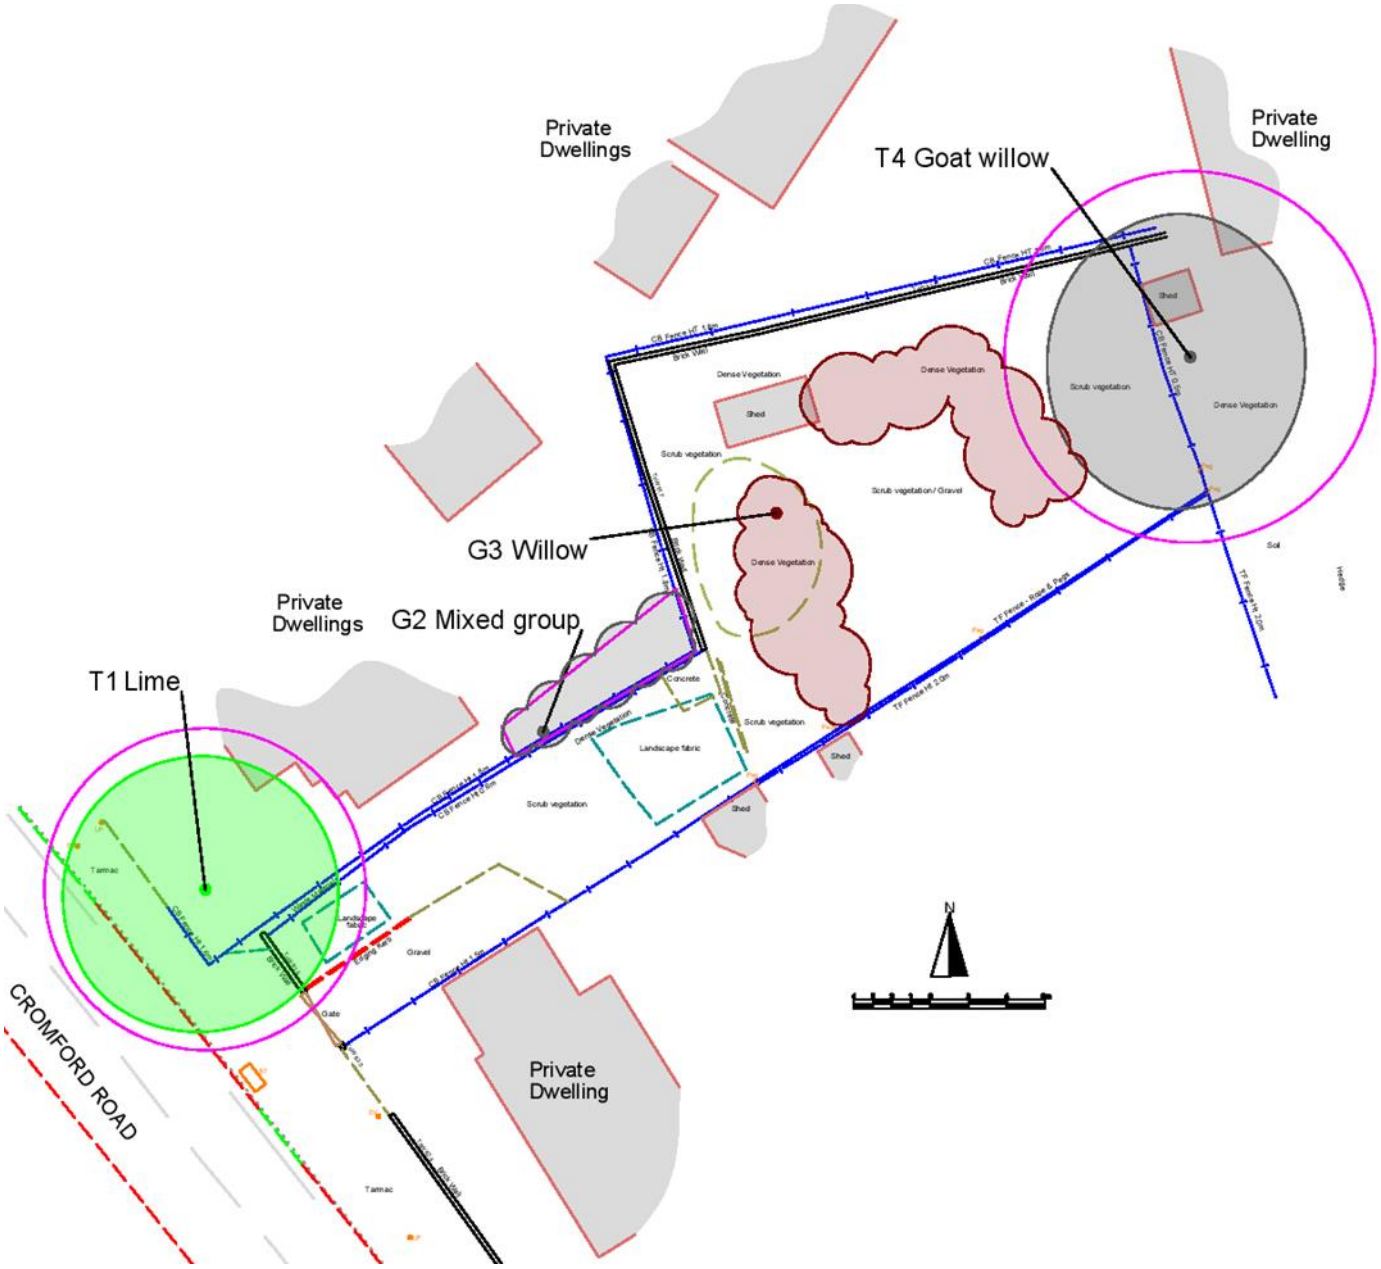

Shaded outline shows tree canopy graded in accordance with BS5837; RPA shown in magenta. The position of the trees is not intended to infer ownership which should be clarified before any tree work is carried out. This tree plan is also supplied as an AutoCAD dwg file, XREFerenced to the topographical model. The tree geometry including the canopy and RPA are stored as layers that can be easily imported and overlaid onto a design layout to produce a tree constraints plan. Note: the CAD drawing units are metres.

© 2010-2026 All rights reserved

Plan ID	Species	Height (m)	Girth (cm)	Diameter (m)	No. of Stems	RPA radius (m) (Area m^2)	Spread (m)	Canopy height (m)	1st sig. branch hght/dir	Life stage Physiol. cond. Structural cond.	Observations, notes & recommendations	Remaining contribution (years)	BS5837 Grading
T1	Lime *Tilia x europaea*	18	219	0.70	1	8.4 (220)	N 7 E 7 S 7.5 W 7.5	3.5	3.5	Early-mature Good Good	T3 of TPO 308/2004	40+	A2
G2	Mixed group	4					N E S W			Mature Good Good	Pyracantha & photinia on a higher level behind a retaining wall.	10+	C2
G3	Willow *Salix spp.*	3					N E S W			Mature Good Poor	Regrowth from felled willow stumps.	<10	U
T4	Goat willow *Salix caprea*	16	254	0.81	1	9.7 (296)	N 7.5 E 6 S 8 W 7.5	1	2	Mature Good Fair	Codominant stems with included bark.	10+	C2

© 2010-2026 All rights reserved

BS 5837:2012 Cascade chart for tree quality assessment

AT2 Tree Surveys


Category and definition	Criteria (including subcategories where appropriate)			Identification on plan
	Trees unsuitable for retention (see Note)			
Category U Those in such a condition that they cannot realistically be retained as living trees in the context of the current land use for longer than 10 years	• Trees that have a serious, irremediable, structural defect, such that their early loss is expected due to collapse, including those that will become unviable after removal of other category U trees (e.g. where, for whatever reason, the loss of companion shelter cannot be mitigated by pruning) • Trees that are dead or are showing signs of significant, immediate, and irreversible overall decline • Trees infected with pathogens of significance to the health and/or safety of other trees nearby, or very low-quality trees suppressing adjacent trees of better quality *NOTE Category U trees can have existing or potential conservation value which it might be desirable to preserve*			Red
	1 – Mainly arboricultural qualities	**2 – Mainly landscape qualities**	**3 – Mainly cultural values, including conservation**	
Trees to be considered for retention				
Category A **Trees of high quality** with an estimated remaining life expectancy of at least 40 years	Trees that are particularly good examples of their species, especially if rare or unusual; or those that are essential components of groups or formal or semi-formal arboricultural features (e.g. the dominant and/or principal trees within an avenue)	Trees, groups or woodlands of particular visual importance as arboricultural and/or landscape features	Trees, groups or woodlands of significant conservation, historical, commemorative or other value (e.g. veteran trees or wood-pasture)	Green
Category B **Trees of moderate quality** with an estimated remaining life expectancy of at least 20 years	Trees that might be included in category A, but are downgraded because of impaired condition (e.g. presence of significant though remediable defects, including unsympathetic past management and storm damage), such that they are unlikely to be suitable for retention for beyond 40 years; or trees lacking the special quality necessary to merit the category A designation	Trees present in numbers, usually growing as groups or woodlands, such that they attract a higher collective rating than they might as individuals; or trees occurring as collectives but situated so as to make little visual contribution to the wider locality	Trees with material conservation or other cultural value	Blue
Category C **Trees of low quality** with an estimated remaining life expectancy of at least 10 years, or young trees with a stem diameter below 150 mm	Unremarkable trees of very limited merit or such impaired condition that they do not qualify in higher categories	Trees present in groups or woodlands, but without this conferring on them significantly greater collective landscape value; and/or trees offering low or only temporary/transient landscape benefits	Trees with no material conservation or other cultural value	Grey

© 2010-2026 All rights reserved

Arboricultural Impact Assessment (AIA)

Impact of the development on the trees

In order to accommodate the two dwelling it will be necessary to remove the willow stumps (G3). All other trees will be retained as shown in the plan below.

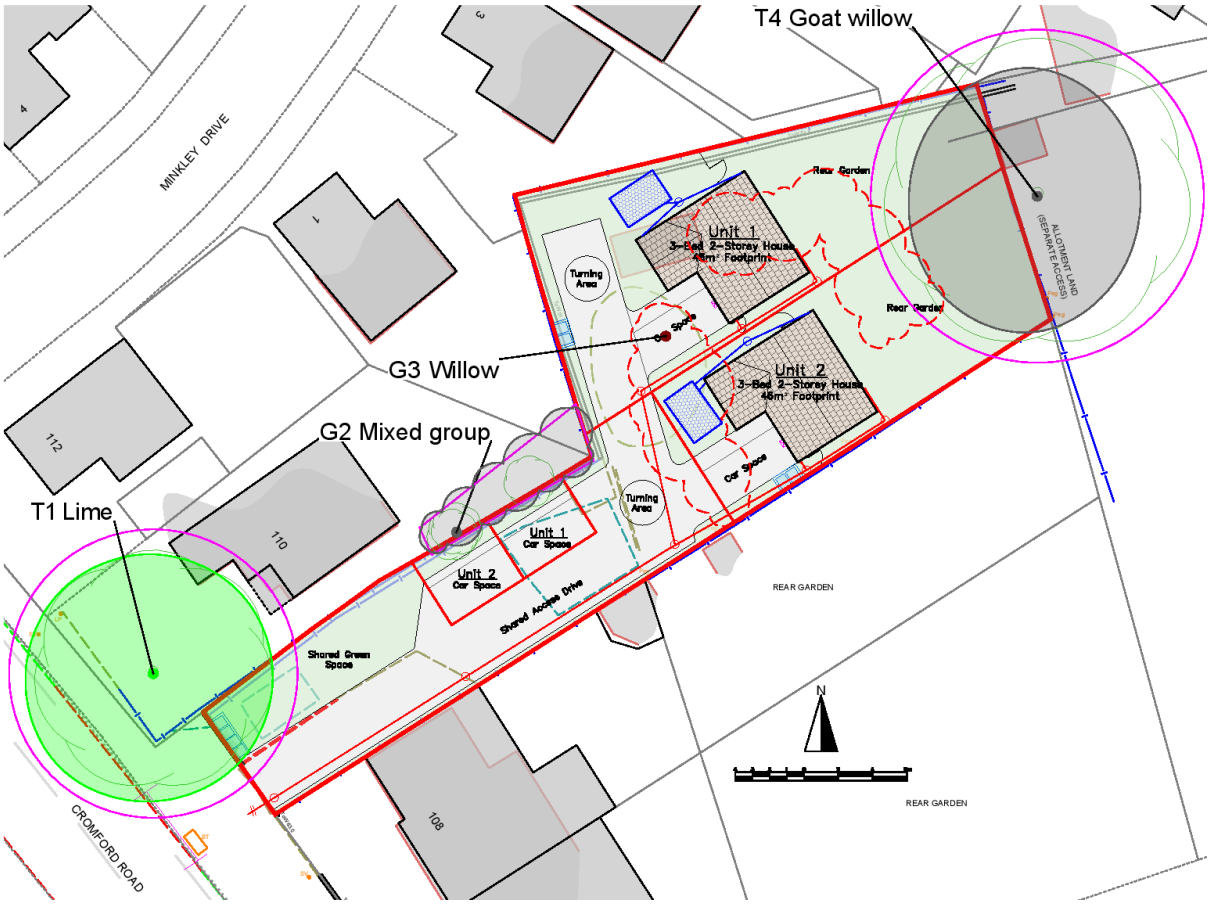

Trees to be removed shown with dashed red outline. Root protection areas shown in magenta. Existing buildings shaded grey.

The mixed group (G2) stands at a higher level behind a retaining wall so the roots are unlikely to be affected by the proposed development.

The footprint of the development is outside of the root protection area of the retained trees so there is no requirement for specially engineered foundations.

There is already hard surfacing over the access which will be reused for the development.

Measures to minimise damage to the retained trees are detailed in the arboricultural method statement below.

Impact of the trees on the development

The design takes into account the size, position and future growth of the trees relative to the properties to minimise issues of shading, seasonal nuisance, frequent remedial pruning or future pressure for removal.

© 2010-2026 All rights reserved

Arboricultural Method Statement (AMS)


Pre-development tree work

Prior to commencement of construction the coppiced willow stumps (G3) will be removed. All works will be carried out in accordance with BS3998: 2010[1]. The tree contractor will carry out checks for nesting birds and bats. The disposal of timber, brash, stumps and other arisings will be agreed with the client. Where stumps are to be removed from within the RPA of retained trees they should be ground out using a stump grinder rather than pulled out with an excavator to avoid damaging the roots of the retained trees.


Construction exclusion zones

Before any development commences, protective barriers will be installed to protect the trunks and lower limbs of the trees and to exclude construction from the root protection area. The position for the barrier is shown in an A1 size 1:100 scaled tree protection plan *"108A Cromford Road, Langley Mill AIA-A1 TPP.pdf",* a section of which is shown overleaf. The radius of the RPA for each tree is shown in the Survey Schedule and on the tree protection plan. Where trees overhang it may be necessary to increase the extent of the tree protection barriers to contain the canopy where it could be damaged by machinery or vehicles. Due to surveying limitations, discrepancies may exist in the relative position of features on the plan, therefore all measurements for RPAs should be taken directly from the trees themselves.

Examples of suitable protective barriers are shown below.

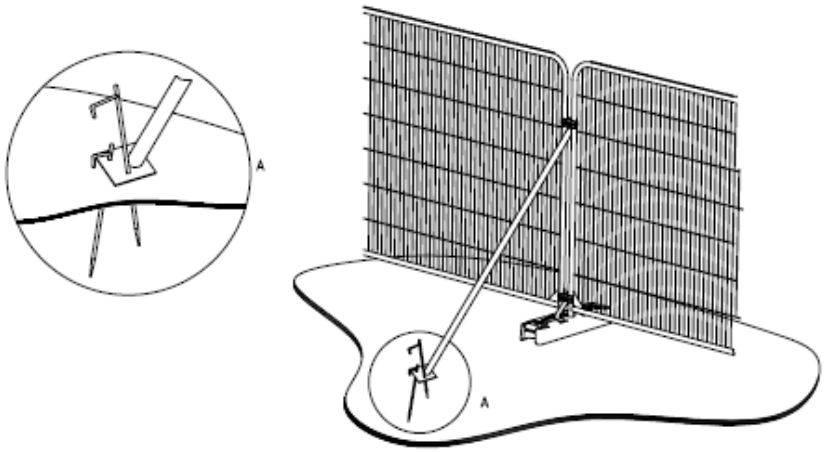

a) Stabilizer strut with base plate secured with ground pins

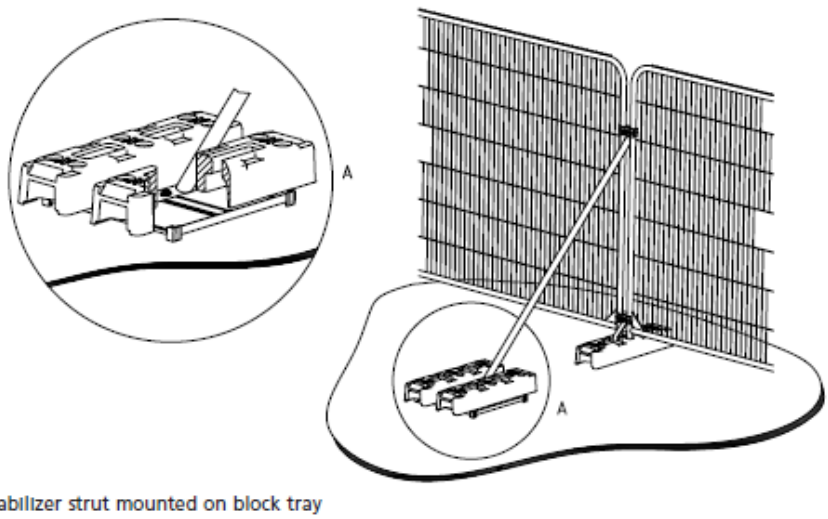

b) Stabilizer strut mounted on block tray



© 2010-2026 All rights reserved

Protective Barrier (British Standard 5837: 2012)

The barrier will have all-weather notices attached with words such as:

"CONSTRUCTION EXCLUSION ZONE – NO ACCESS".

Barriers should be fit for the purpose of excluding construction activity and appropriate to the degree and proximity of work taking place around the retained tree(s). Barriers should be well braced to resist impacts and maintained to ensure that they remain rigid and complete.

The protected area should be regarded as sacrosanct, and barriers and ground protection should not be removed or altered without prior recommendation by the project arboriculturist and, where necessary, approval from the local planning authority. All barriers will remain in place until completion of all works.

Further guidance can be found by following the link for *Fencing protected trees* on page 24.



Extract from the tree protection plan showing siting of protective fencing.

Foundation construction

To minimise future risk of subsidence and/or heave, the foundations will be constructed in accordance with NHBC Standards Part 4 (2021). *Chapter 4.2 Building near trees*[3].

The foundations will be outside of the RPA of the retained trees so special foundations will not be required and conventional strip foundations will be used.

Routing of services

Early consultation and collaboration regarding the planning of utility runs is recommended so that underground services avoid the RPA.

© 2010-2026 All rights reserved

Services will be connected to the existing service runs and any new services will be routed either outside of the RPA or by using trenchless techniques such as moling or air-spading. If moling, entry and retrieval pits will be outside of the RPA.

Further guidance can be found in the Street Works UK: Publications Volume 4: *Guidelines for the Planning, Installation and Maintenance of Utility Apparatus in Proximity to Trees*[4] and by following the link for *Installing services in root protection areas* on page 24.

Hard surfacing

There is an existing hard surface providing access to the site which will be reused for the two dwellings, perhaps with a new wearing surface.

The bin store close to Cromford Road is within the RPA of the neighbouring lime (T1). The base for the bin store will be constructed using "no-dig" methods and will be gas and water permeable throughout its design life. New permanent hard surfacing should not exceed 20% of any existing unsurfaced ground within the RPA.

Guidance can be found in Guidance Note 12: *The Use of Cellular Confinement Systems Near Trees: A Guide to Good Practice*[5] from where the following key points have been taken.

The three principles of no-dig construction are:


- Roots must not be severed.
- Soil must not be compacted.
- Oxygen must be able to diffuse into the soil (and carbon dioxide out of the soil) beneath the engineered surface.

A cellular confinement system is a series of geocells arranged in a honeycomb-like formation that is combined with an underlying geotextile and angular stone to spread loads in such a way as to minimise compaction of underlying soil. Wearing surface options include porous asphalt, permeable block paving and loose or resin-bound gravel.



When cellular confinement systems or 'geocells' are used to protect tree root zones the central concept is that they are installed above ground and this normally results in a surface that is around 150mm above the existing ground level for footpaths, and in excess of 300mm above for roads and driveways. Careful consideration may need to be given to matching the raised level with existing surfaces and a sectional drawing can be useful.

© 2010-2026 All rights reserved

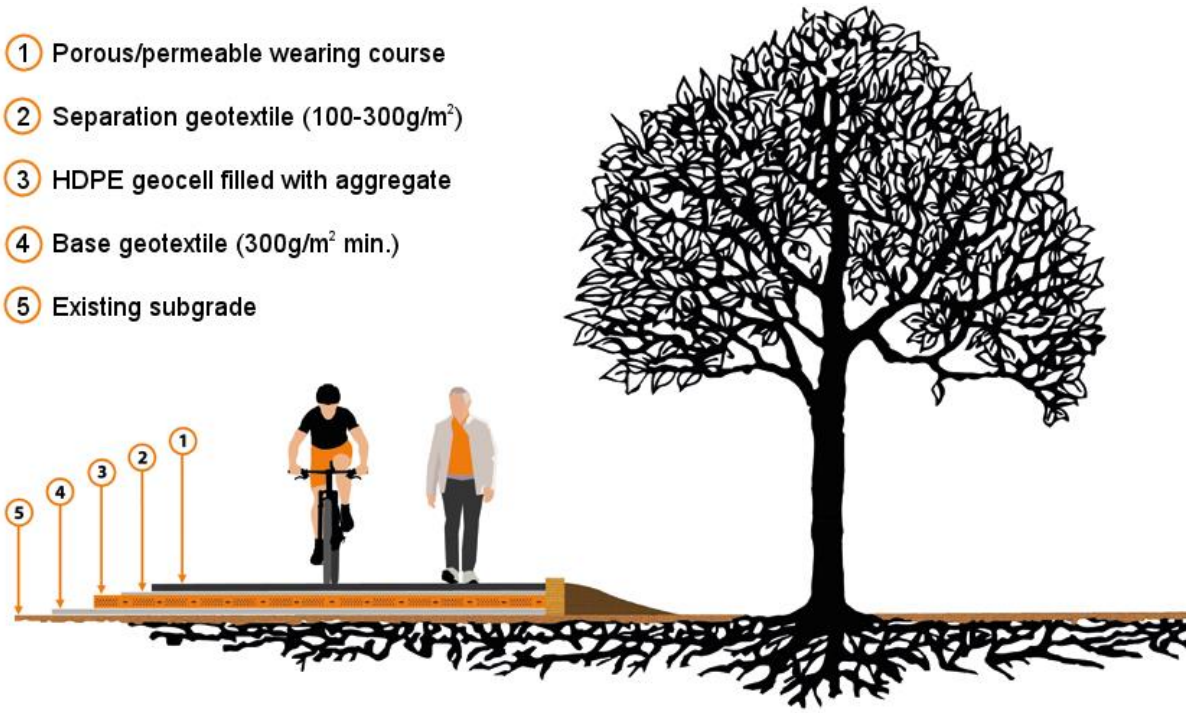

The basic approach to using cellular confinement systems for ground protection near trees[5].

A suitably qualified technician should specify the appropriate depth of geocell to use and this will depend on the bearing capacity and the strength of the soil.

The design should not require excavation into the soil but if there are no obvious surface roots the removal of up to 50mm of the turf layer or any other surface vegetation may be removed. A tracked excavator with a toothless grading bucket is normally the best machine to use to remove the turf layer because this creates an even surface. For this application excavators should be of an appropriate size for delicate works (i.e. ≤5 tonne). Ground preparation works using excavators in root protection areas must be supervised by an arboriculturist to make sure that significant roots (single roots >25mm diameter or clusters of roots 10–25mm in diameter) are preserved and to ensure that vehicles are being used appropriately.

It is important to prevent compaction within the RPA during the geocell installation. This can be achieved either by carrying out work progressively from the newly-laid surface or by installing a temporary, non-compressible protective layer over the RPA.

There are several proprietary geocell systems that allow pedestrian and vehicular surfaces to be laid within the RPA. Further details can be obtained from companies including Geosynthetics Cellweb and Terram Geocell. Selection of the geocell supplier is a commercial decision. Suppliers have technical specialists that can assist with the development of the geocell specification including the surface finish and the (no-dig) edging.

Further guidance can be found by following the link for *Installing/upgrading surfacing in root protection areas* on page 24.

Other measures

- To avoid contamination and compaction, no materials will be stored within 10 metres of a tree trunk or on any unprotected soil surfaces. This includes building materials, scaffolding, fuel, site huts and temporary toilets.
- No mixing or storage of materials will take place up a slope where they may leak down into an RPA. Where the contours of the site create a risk of harmful spillages running into RPAs,

© 2010-2026 All rights reserved

precautionary measures such as sandbags and heavy-duty plastic sheeting will be installed to prevent contamination. (see also link to *Pollution control* on page 24)

- Due to the highly alkaline leachate produced during the curing of wet concrete, concrete will not be poured within the root protection area (RPA) unless an impermeable liner has been installed.
- Notice boards will not be attached to any part of a tree and no fires will be allowed within 10 metres of the canopy or the protective barrier of any retained tree.
- Screw piles are preferred for any fencing installed within the RPA of any tree. Initially the post holes must be carefully dug by hand and positioned so that no roots greater than 25mm in diameter are severed. As above, post-fixing concrete will not be used unless an impermeable liner has been installed.

Sequence of works

1) Pre-development tree work to remove trees identified in the Arboricultural Impact Assessment (AIA).
2) Installation of protective fencing to establish construction exclusion zones.
3) Site development including routing of services and installation of hard surfacing.
4) Removal of protective fencing and ground protection.

Monitoring

The main contractor will be responsible for:

- Monitoring of all operations with regard to tree protection on site.
- Maintaining the integrity of all tree protection measures.
- Keeping a copy of the tree protection plan on site for reference during construction.
- Maintaining an auditable system of arboricultural site monitoring, which should extend to arboricultural supervision whenever construction and development activity is to take place within or adjacent to any RPA.
- The induction of staff and contractors.
- The compliance of sub-contractors.
- Ensuring that the planning conditions attached to the planning consent are adhered to at all times.
- Further guidance can be found by following the link for *Monitoring protection* on page 24.



© 2010-2026 All rights reserved


Appendix A – Glossary of arboricultural terms

Access facilitation pruning

One-off tree pruning, without significant adverse impact on tree physiology or amenity value, which is directly necessary to provide access for operations on site.

Arboricultural impact assessment (AIA)

Study to identify and evaluate the direct and indirect impacts on existing trees that may arise as a result of the implementation of a site layout proposal.

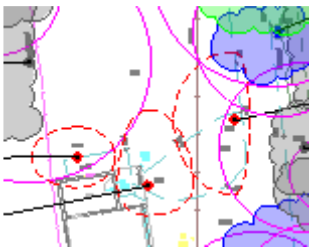

Arboricultural method statement (AMS)

Details of methodologies to be implemented in order to protect the retained trees **(see also tree protection plan (TPP)**).

Codominant stems

Codominant stems occur when a tree grows with two or more main stems or 'leaders' that are about the same diameter and emerge from the same location on the main trunk. The bark for each stem is trapped inside the fork preventing them from fusing together. This may also be referred to as a compression fork.

The presence of codominant stems with included bark reduces the strength of the union and therefore increases the risk of failure under loading during strong winds[15].

However, the presence of included bark does not mean the tree will fail. Codominant stems are a common feature of many trees and most will live to the end of their natural life without a problem. The decision whether to take remedial action should take a range of factors into consideration including the size, position and condition of the tree and the proximity of 'targets' close to the tree.



Construction exclusion zone (CEZ)

An area based on the **RPA** to be protected during development by the use of barriers and/or ground protection to ensure the long-term retention of a tree.

Crown lifting

The removal of lower branches and/or parts of pendulous upper branches to provide clearance over roads and paths and allow more light under a tree or into nearby property.

Work specified as a clearance height above ground level.



© 2010-2026 All rights reserved

Crown reduction

The cutting back of branches to reduce the overall size of a tree's canopy. Crown reduction should seek to retain the tree's natural form and a flowing branch line without leaving stumps.

Work specified as a reduction in height and radial width and/or annotated photographs.



Drop crotch pruning

Removing a portion of a branch or stem by cutting back to a lateral branch which is at least 1/3 of the diameter of the section that is being removed.



Epicormic growth

Bushy shoots growing directly from the trunk arising from adventitious or dormant buds.

Formative pruning

Pruning of young trees to produce a good shape and prevent future management problems.

Hanger

A broken branch lodged or hanging in the canopy.

No-dig construction

With reference to foundations, hard surfacing and utilities, the design should not require excavation into the soil, including through lowering of levels and/or scraping, other than the removal, using hand tools or an air-spade, of any turf layer or other surface vegetation.

Pile and beam foundation

Type of foundation where mini-piles or screw piles are bridged with concrete and/or steel beams and the floor suspended using block and beam construction with a vented void below. The underside of the beams is at or just above ground level. Often used where conventional strip foundations would cause unacceptable root damage.



Pollarding and Coppicing

The removal of all or nearly all of a tree's branches and foliage. Pollarding is generally only appropriate on trees where the practice has been long established and carried out regularly such as willow, lime and plane.

A framework pollard removes all the smaller branches but leaves a framework of major limbs.


With coppicing trees or shrubs are cut close to ground level and allowed to regenerate.



© 2010-2026 All rights reserved

Root protection area (RPA)

The minimum area around a tree deemed to contain sufficient roots and rooting volume to maintain the tree's viability, and where the protection of the roots and soil structure is treated as a priority (shown in magenta in the tree survey plan on page 12).



Ruderals

A ruderal species is a plant species that is first to colonize disturbed lands such as construction sites.

Sucker growth

Similar to epicormic growth but suckers shoot from the roots of the parent tree.

Target pruning

Pruning to create or maintain clearance from buildings, street lights, guttering, aerials, etc.


Topographical survey

An accurate depiction of an area of land which is scaled and detailed to show all the natural and manmade features and their levels.




Tree constraints plan (TCP)

Scale drawing showing the canopy and RPA of the trees overlaid onto the layout scheme to highlight potential conflict. The TCP may include shading modelling.



Tree protection plan (TPP)

Scale drawing showing finalised layout, tree retention and tree protection measures detailed in the **arboricultural method statement (AMS)**.

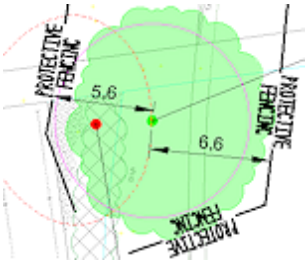

© 2010-2026 All rights reserved

Appendix B – Site guidance notes

Barrell Tree Consultancy has produced a series of site guidance notes that give more detail on specific elements of the management of trees on construction sites. They can be downloaded using this link to their website or by using the QR codes or links below.



1. Monitoring protection
   https://www.barrelltreecare.co.uk/resources/technical-guidance/sgn01/



2. Fencing protected trees
   https://www.barrelltreecare.co.uk/resources/technical-guidance/sgn02/



3. Ground protection
   https://www.barrelltreecare.co.uk/resources/technical-guidance/sgn03/



4. Pollution control
   https://www.barrelltreecare.co.uk/resources/technical-guidance/sgn04/



5. Site cranes and piling rigs
   https://www.barrelltreecare.co.uk/resources/technical-guidance/sgn05/



6. Height restrictions
   https://www.barrelltreecare.co.uk/resources/technical-guidance/sgn06/



7. Excavation in root protection areas
   https://www.barrelltreecare.co.uk/resources/technical-guidance/sgn07/



8. Removing surfacing and structures in root protection areas
   https://www.barrelltreecare.co.uk/resources/technical-guidance/sgn08/



9. Installing/upgrading surfacing in root protection areas
   https://www.barrelltreecare.co.uk/resources/technical-guidance/sgn09/



10. Installing structures in root protection areas
    https://www.barrelltreecare.co.uk/resources/technical-guidance/sgn10/



11. Installing services in root protection areas
    https://www.barrelltreecare.co.uk/resources/technical-guidance/sgn11/



12. Landscaping in root protection areas
    https://www.barrelltreecare.co.uk/ resources/technical-guidance/sgn12/

© 2010-2026 All rights reserved

Appendix C – Bibliography & References

1 British Standards Institution, (2010). *BS 3998: 2010 – Recommendations for tree work*. Milton Keynes: BSI

2 British Standards Institution, (2012). *BS 5837: 2012 – Trees in relation to design, demolition and construction – Recommendations*. Milton Keynes: BSI

3 NHBC Standards Part 4 (2026). *Chapter 4.2 Building near trees.* National House Building Council.

4 Street Works UK: Publications Volume 4 – *Guidelines for the planning, installation, and maintenance of Utility apparatus in proximity to Trees.* Street Works UK.

5 Rose, B. (2020). *The Use of Cellular Confinement Systems Near Trees: A Guide to Good Practice*. Guidance Note 12. Arboricultural Association.

6 Crow, P. (2005). *The Influence of Soils and Species on Tree Root Depth*, Forestry Commission Information Note, Forestry Commission, Edinburgh.

7 Dobson, M. (1995). *Tree Root Systems*. Arboricultural Advisory Information Service 130/95/ARB

8 John Roberts, Nick Jackson & Mark Smith (2006). *Tree Roots in the Built Environment*. Arboricultural Association.

9 Trees & Design Action Group (TDAG), (2021). *Trees, planning and Development – A Guide for Delivery*. https://www.tdag.org.uk/

10 Strouts, R. G. & Winter, T. G. (2000). 2nd ed. *Diagnosis of Ill Health in Trees.* The Stationery Office.

11 Mattheck, C. & Breloer, H. (2006). *The Body Language of Trees, A Handbook for Failure Analysis.* The Stationery Office.

12 Lonsdale, D. (2021). *Principles of Tree Hazard Assessment and Management*. Arboricultural Association.

13 Cavanagh v Witley Parish Council (1) and D Kevin Shepherd (t/a Shepherd Tree Surgeons & Forestry Contractors) (2) [2017]

14 Shigo, A. L. (1991). 3rd ed. Modern Arboriculture. Shigo & Trees, Associates.

15 Smiley, E. T. Does Included Bark Reduce the Strength of Codominant Stems?, *Journal of Arboriculture 29(2),* March 2003, pages 104-106

16 Guy Watson & Ted Green. *Fungi on Trees – An Arborists Field Guide* (2011) Arboricultural Association



© 2010-2026 All rights reserved
